Government eProcurement System

eProcurement System Government of India

Published Corrigendum Details

Date : 10-Nov-2026 01:13 PM

Print

Organisation Chain :	NHPC Limited||Corporate Office-Faridabad-NHPC||Contract-E and M-CO-NHPC
Tender ID :	2026_NHPC_906114_1
Tender Ref No :	NH/Conts(EnM)-III/Uri-I Stage-II/ENM/2026/01
Tender Title :	Lot-III Electro-mechanical works package of 240 MW (2X120MW) Uri-I Stage-II H.E Project, Baramulla District of UT of J and K
Corrigendum Type :	Date

Corrigendum:10

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 13	Extension in Critical Dates of Tender and amendment in IFB	10-Nov-2026 01:12 PM	Corrigendum13.pdf	582.76

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	25-Nov-2026 05:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	24-Nov-2026 02:30 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	24-Nov-2026 02:30 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:9

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
CorrigendumNo12.pdf	Extension in critical dates of Tender	29-Oct-2026 07:20 AM	CorrigendumNo12.pdf	341.1

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	11-Nov-2026 05:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	10-Nov-2026 02:30 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	10-Nov-2026 02:30 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:8

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 10	Date Extension	14-Oct-2026 03:51 PM	CorrigendumNo10.pdf	176.1

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	30-Oct-2026 05:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	29-Oct-2026 02:30 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	29-Oct-2026 02:30 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:7

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 09	Date Extension	26-Sep-2026 10:24 AM	CorrigendumNo9.pdf	176.37

Critical Dates			
Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	16-Oct-2026 05:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	15-Oct-2026 02:30 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	15-Oct-2026 02:30 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:6

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 07	Date Extension	08-Sep-2026 04:40 PM	CorrigendumNo7.pdf	176.24

Critical Dates			
Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	29-Sep-2026 05:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	28-Sep-2026 02:30 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	28-Sep-2026 02:30 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:5

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 06	Date Extension	25-Aug-2026 10:44 AM	CorrigendumNo6.pdf	131.87

Critical Dates			
Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	11-Sep-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	09-Sep-2026 06:00 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	09-Sep-2026 06:00 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:4

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 05	Date Extension	07-Aug-2026 06:28 PM	Corri5.pdf	115.37

Critical Dates			
Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	28-Aug-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	25-Aug-2026 06:00 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	25-Aug-2026 06:00 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:3

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 03	Extension of Critical Dates of Tender	10-Jul-2026 11:51 AM	CorrigendumNo3.pdf	71.6

Critical Dates			
Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	14-Aug-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	10-Aug-2026 06:00 PM

Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	24-Jul-2026 06:55 PM	**Bid Submission End Date**	10-Aug-2026 06:00 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:2

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No 2	Extension of Online Bid Submission Start Date	03-Jul-2026 05:01 PM	CorrigendumNo2.pdf	65.86

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	29-Jul-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	24-Jul-2026 06:00 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	10-Jul-2026 06:55 PM	**Bid Submission End Date**	24-Jul-2026 06:00 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Corrigendum:1

Corrigendum Title	Corrigendum Description	Published Date	Document Name	Doc Size(in KB)
Corrigendum No.1	Pre bid Conference date extension	17-Jun-2026 05:56 PM	CorrigendumNo1.pdf	70.62

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	29-Jul-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	24-Jul-2026 06:00 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	03-Jul-2026 06:55 PM	**Bid Submission End Date**	24-Jul-2026 06:00 PM
Pre Bid Meeting Date	29-Jun-2026 02:30 PM		

Details Before Corrigendum

Critical Dates

Publish Date	29-May-2026 06:55 PM	**Bid Opening Date**	29-Jul-2026 03:30 PM
Document Download/Sale Start Date	29-May-2026 06:55 PM	**Document Download/Sale End Date**	24-Jul-2026 06:00 PM
Clarification Start Date	29-May-2026 06:55 PM	**Clarification End Date**	12-Jun-2026 05:00 PM
Bid Submission Start Date	03-Jul-2026 06:55 PM	**Bid Submission End Date**	24-Jul-2026 06:00 PM
Pre Bid Meeting Date	19-Jun-2026 02:30 PM		

Corrigendum No. 13

(Extension in Critical dates of Tender & amendment in IFB)

Description of Work: Lot-III: Electro-mechanical works package of 240 MW (2X120MW) Uri-I Stage-II H.E Project, Baramulla District of UT of J&K, India

Tender ID.: 2026_ NHPC_906114_1

	Description of referred clause	Referred Clause No.	Existing Clause of Tender Document	Modified provision of Tender Document
A.	**Volume-I-IFB (Information for Bidders)**			
1.	**Construction Schedule:**	**IFB Cl. No.19. :**	19. Construction Schedule: i) Project completion period is 44 months from project zero date (Project zero date: Date of award of civil works-Lot-I (Letter Of Award for Civil Work issued on 28.03.2026). ii) The E&M package works shall commence after 6 months from award of civil package. iii) The total time period for E&M works is 38 months. The proposed construction schedule is attached at Annexure-I for reference.	Sl. No. 19' Construction Schedule' is deleted and replaced as under : 19. Construction Schedule: i) Project completion period is 44 months from project zero date (Project zero date: Date of award of civil works-Lot-I (Letter Of Award for Civil Work issued on 28.03.2026). ii) The total time period for E&M works is 38 months. The proposed construction schedule is attached at Annexure-I for reference.
B.	**NIT- Vol.0**			

<table>
<tr><th></th><th>Description of referred clause</th><th>Referred Clause No.</th><th>Existing Clause of Tender Document</th><th>Modified provision of Tender Document</th></tr>
<tr><td>2.</td><td>Critical Dates of Tender</td><td>NIT Clause No.1.2</td><td>
<table>
<tr><th>Sl. No.</th><th>Particulars</th><th>Date & Time</th></tr>
<tr><td>(vi)</td><td>Document Download End Date & Time</td><td>10/11/2026 14:30 Hrs. (IST)</td></tr>
<tr><td>(vii)</td><td>Online Bid Submission End Date & Time</td><td>10/11/2026 14:30 Hrs. (IST)</td></tr>
<tr><td>(viii)</td><td>Last date of submission of Tender fee, EMD (Bid Security) and other offline supporting document(s) at “General Manager, Contract (E&M)-III, 2nd Floor, Jyoti Sadan, NHPC Office Complex, Sector-33, Faridabad-121003 (Haryana)</td><td>10/11/2026 18:00 Hrs. (IST)</td></tr>
<tr><td>(ix)</td><td>Bid Opening Date & Time
i. Technical bid
ii. Price bid</td><td>11/11/2026 17:30 Hrs. (IST)
To be intimated separately.</td></tr>
</table>
</td><td>
<table>
<tr><th>Sl. No.</th><th>Particulars</th><th>Date & Time</th></tr>
<tr><td>(vi)</td><td>Document Download End Date & Time</td><td>24/11/2026 14:30 Hrs. (IST)</td></tr>
<tr><td>(vii)</td><td>Online Bid Submission End Date & Time</td><td>24/11/2026 14:30 Hrs. (IST)</td></tr>
<tr><td>(viii)</td><td>Last date of submission of Tender fee, EMD (Bid Security) and other offline supporting document(s) at “General Manager, Contract (E&M)-III, 2nd Floor, Jyoti Sadan, NHPC Office Complex, Sector-33, Faridabad-121003 (Haryana)’
e-Mail: nalinikantverma@nhpc.in</td><td>24/11/2026 18:00 Hrs. (IST)</td></tr>
<tr><td>(ix)</td><td>Bid Opening Date & Time
i. Technical bid
ii. Price bid</td><td>25/11/2026 17:30 Hrs. (IST)
To be intimated separately.</td></tr>
</table>
</td></tr>
</table>

A other terms & conditions of the bid document shall remain unchanged.

Sd/-

General Manager,
Contracts (E&M)-III,
NHPC Limited

URI-1 STAGE-II H E PROJECT

CONSTRUCTION SCHEDULE- ELECTRO-MECHANICAL WORKS

Annexure-I of IFB

10-Nov-26 09:52

#	Activity ID	Activity Name	Original Duration
1	**Uri-1 St-2 240 MW- E&M Package Intergrated Schedule**		1336
2	**Mobilisation**		0
3	MB100	Award date of Civil works	0
4	**Interdependent Milestones**		720
5	**Civil Interface**		720
6	MSC100	Completion of Excavation of Power House	0
7	MSC120	Completion of construction of EOT crane columns & Beams in Service Bay	0
8	MSC130	Completion of construction of EOT crane column & beams in Unit-1	0
9	MSC160	Completion of Excavation of Transformer cavern& Busducts	0
10	HM interface		20
11	MSHM 100	Completion of HM works	0
12	MSHM110	Filling of Water conductor system	20
13	**E&M Works**		1157
14	**Engineering & Supply**		1021
15	EMS100	Design Drawings , Procurement, Fabrication and supply	1021
16	**EOT Crane works**		366
17	EOT100	Supply of EOT crane (150T/25T/15T)	215
18	EOT110	Erection of EOT crane in Service Bay	60
19	EOT120	Extension of EOT crane in U#1 area	5
20	EOT130	Extension of EOT crane in U#2 area	5
21	**Machine Erection**		665
22	Unit-1		635
23	Assembly of Stator & Rotor U#1		635
24	EMU100	Rotor Assembly at Service Bay,U#1	90
25	EMU110	Stator Assembly at Service Bay,U#1	120

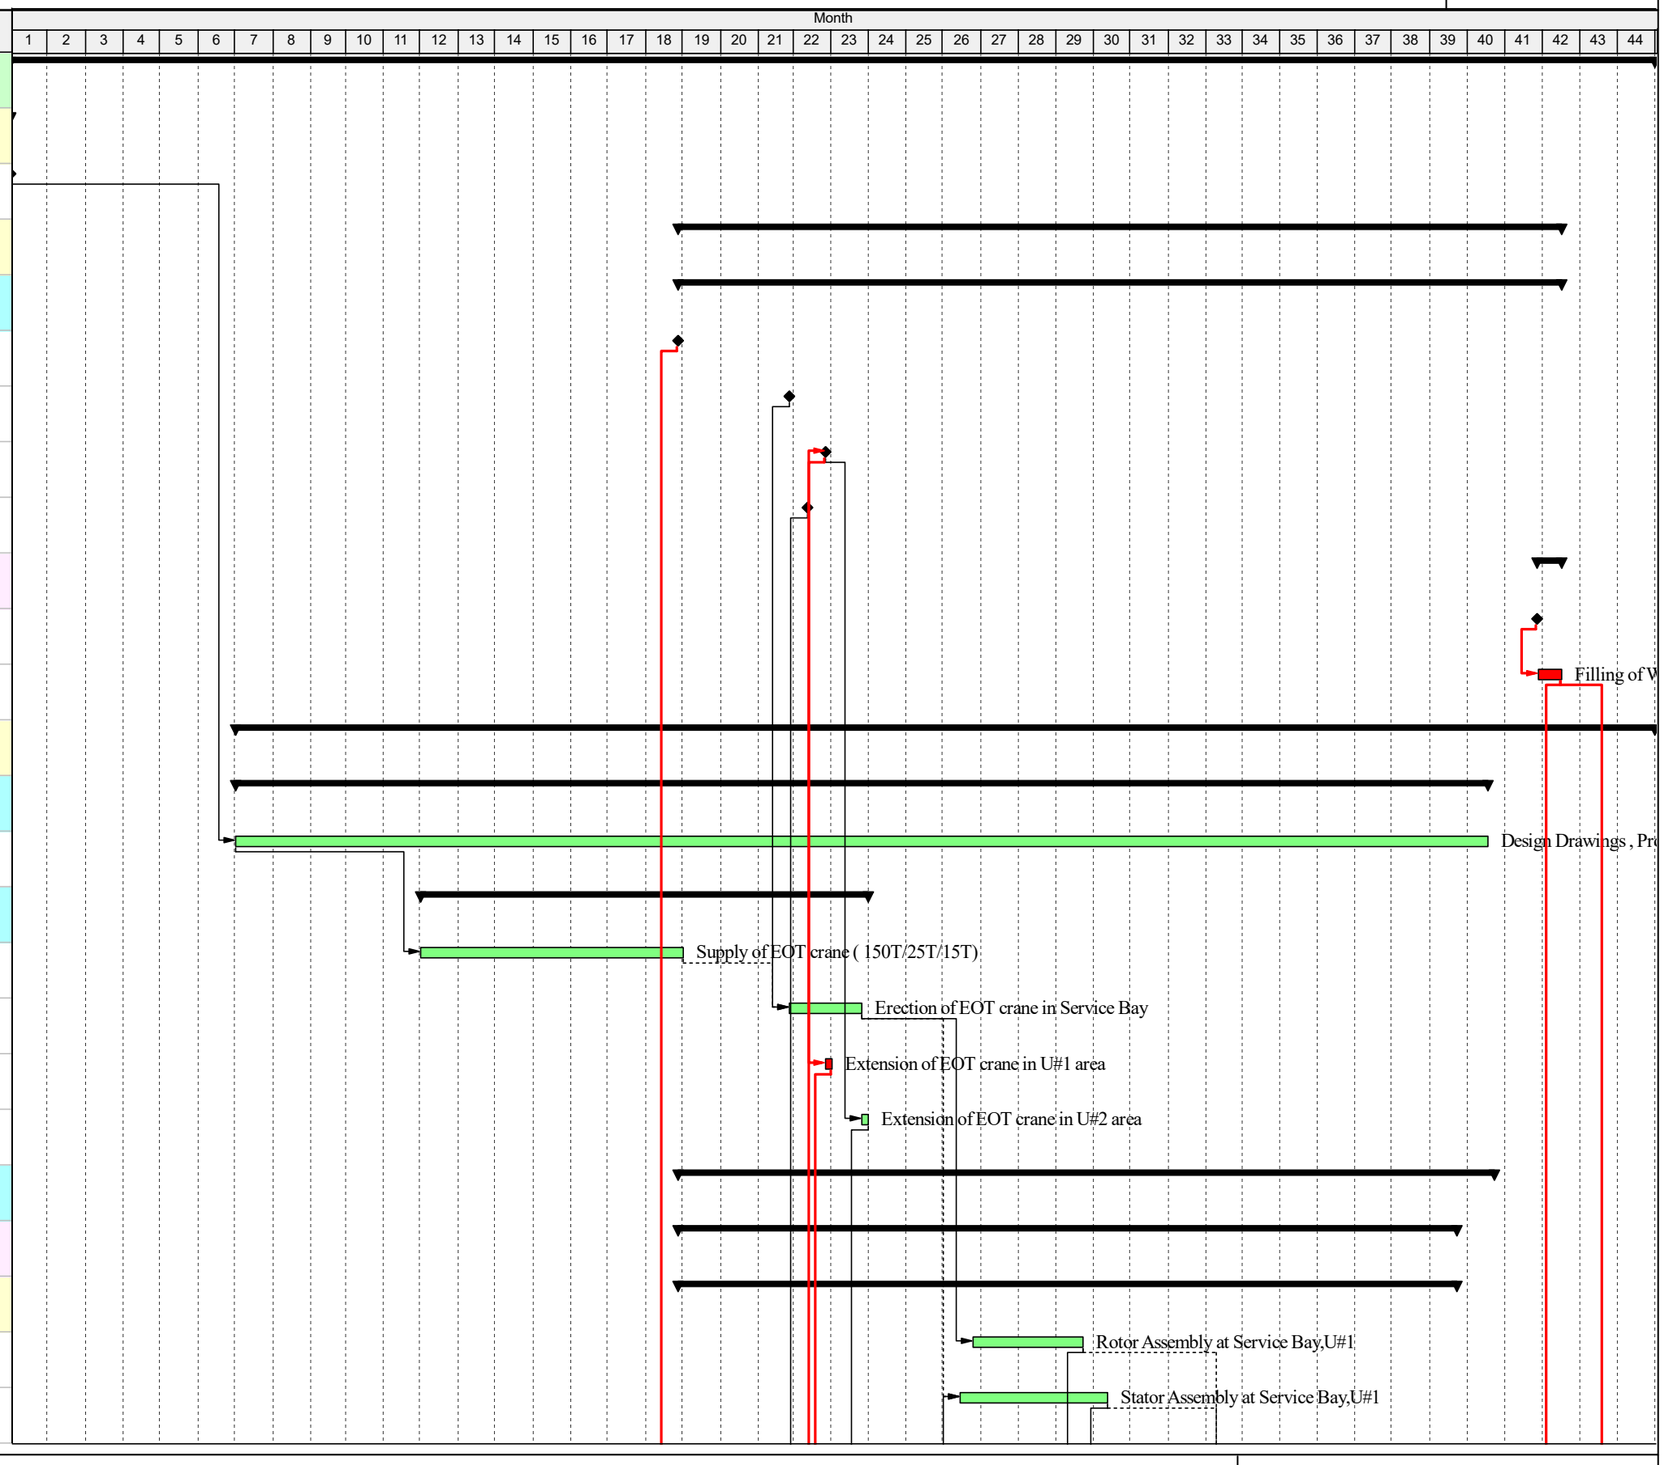

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Note:

1. Project completion period is 44 months from project zero date (Project zero date: Date of award of civil works)
2. The total time period for E&M work is 38 months.
3. Time duration for activities is shown from project zero date , E&M Contractor may modify duration to match 38 month schedule.

TASK filter: All Activities

© Oracle Corporation

PROJECT MONITORING & SUPPORT GROUP (PMSG)

#	Activity ID	Activity Name	Original Duration
26		Erection of E&M components U#1	635
27	EMU1000	Laying of Earthmat, Concreting of Raft upto Draft Tube-1 Bottom	60
28	EMU1100	Erection of Draft Tube U#1 Liners	60
29	EMU1110	Concreting upto Spiral-1 Bottom (By Civil contractor)	45
30	EMU1200	Erection and Testing of Spiral Casing-1	120
31	EMU1250	Handing over of Generator Barrel U#1 for Machine Erection(By Civil Contractor)	75
32	EMU1300	Erection of MIV, Turbine & Generator U#1	210
33	EMU1400	Boxing up of U#1	60
34		Unit-2	575
35		Assembly of Stator & Rotor U#2	140
36	EMU1631	Rotor Assembly at Service Bay U#2	90
37	EMU1632	Stator Assembly at Service Bay U#2	120
38		Erection of E&M components U#2	575
39	EMU1633	Laying of Earthmat, Concreting of Raft upto Draft Tube-2 Bottom	60
40	EMU1634	Erection of Draft Tube U#2 Liners	90
41	EMU1635	Concreting upto Spiral-2 Bottom (By Civil contractor)	45
42	EMU1636	Erection and Testing of Spiral Casing	90
43	EMU1637	Handing over of Generator Barrel U#2 for Machine Erection(By Civil Contractor)	75
44	EMU1640	Erection of MIV, Turbine & Generator U#2	210
45	EMU1650	Boxing up of U#2	60
46		Common Auxiliaries	90
47	CA1620	Erection of Common Auxiliaries	90
48		**Transformer, GIS, XLPE & Pothead Yard works**	560
49	A1000	Completion of Raft & Fire wall in Transformer Cavern (By Civil Contractor)	210
50	A1010	Erection of Transformer	240
51	A1020	Completion of concreting of GIS floor (By Civil Contractor)	90
52	A1030	Erection of GIS including GIS EOT	150

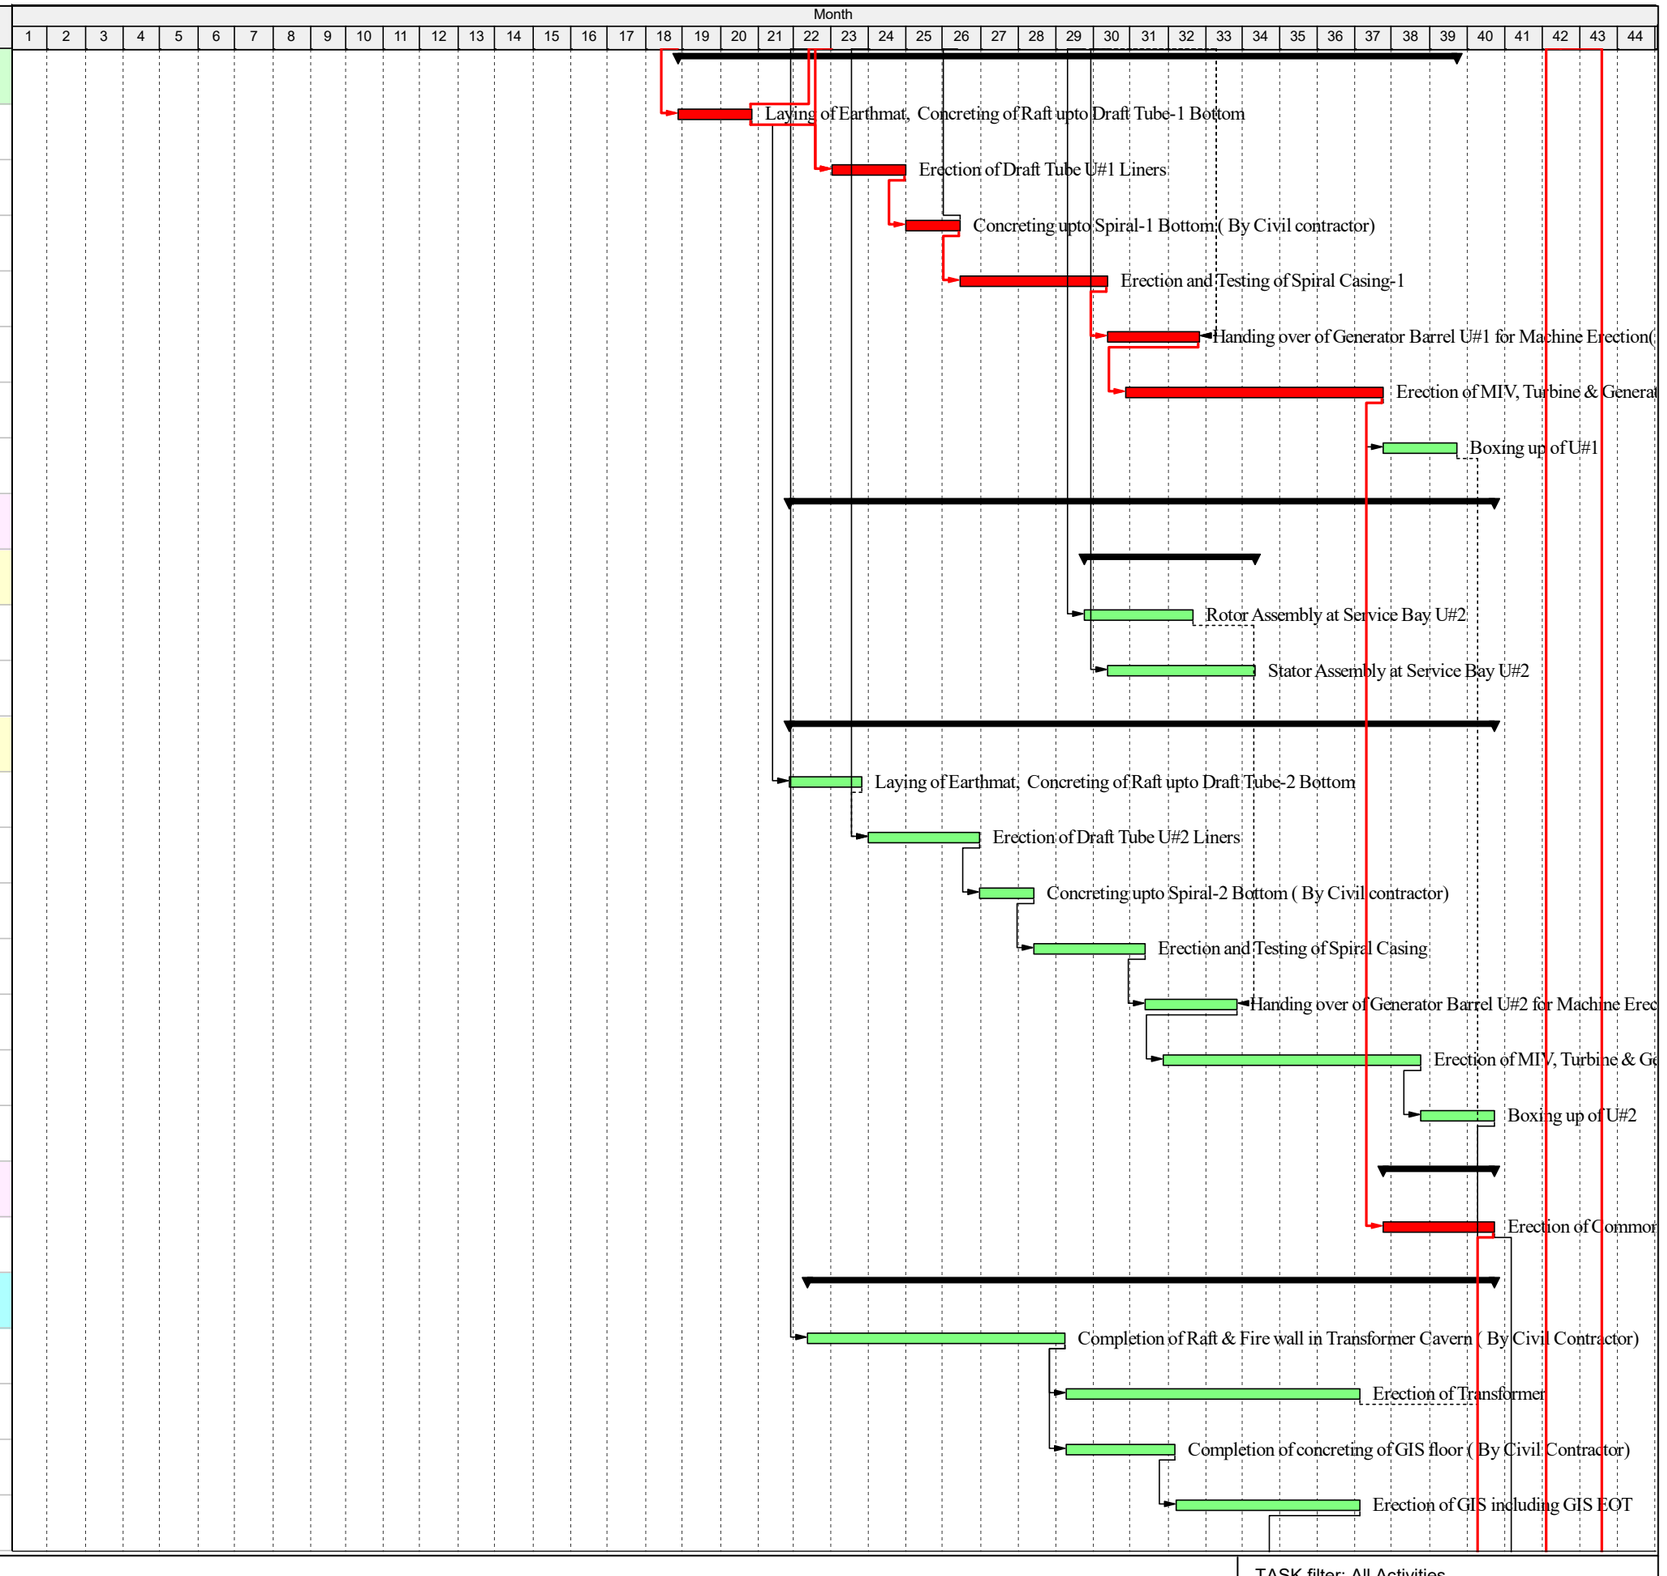

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Note:
1. Project completion period is 44 months from project zero date (Project zero date: Date of award of civil works)
2. The total time period for E&M work is 38 months.
3.Time duration for activities is shown from project zero date , E&M Contractor may modify duration to match 38 month schedule.

TASK filter: All Activities

© Oracle Corporation

#	Activity ID	Activity Name	Original Duration
53	A1040	Laying of XLPE cable	120
54	A1050	Erection of Potheadyard HV Bushing	60
55	**Commissioning**		131
56	Unit-1		101
57	MC1320	Pre-Commissioning of U#1	56
58	MC1330	Testing and Commissioning of U#1	45
59	Unit-2		131
60	MC1350	Pre-Commissioning of U#2	50
61	MC1360	Testing and Commissioning of U#2	30

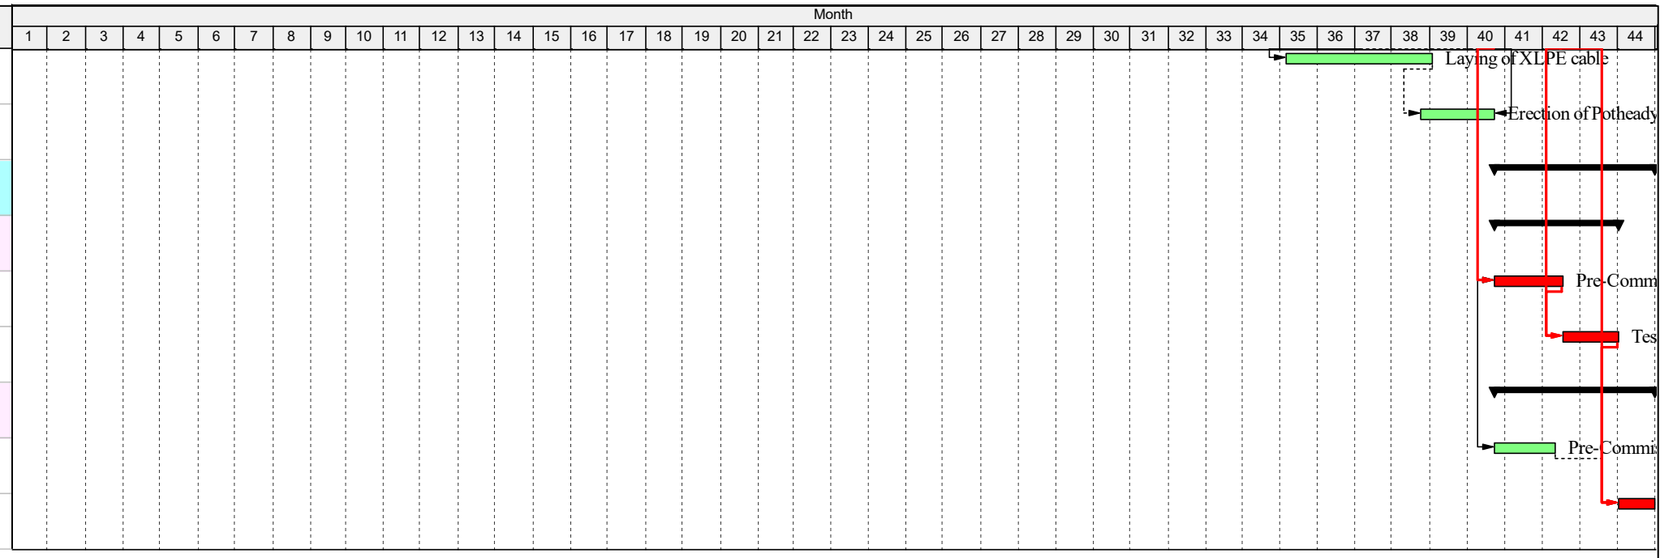

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Note:
1. Project completion period is 44 months from project zero date (Project zero date: Date of award of civil works)
2. The total time period for E&M work is 38 months.
3.Time duration for activities is shown from project zero date , E&M Contractor may modify duration to match 38 month schedule.

TASK filter: All Activities

© Oracle Corporation
